



BOND 2016

Monthly Project Status

January 2019

1) COMPLETED PROJECTS

1. **New Administration Building**
2. **High School Softball Batting Cages**
3. **Tennis Court Improvements**
4. **Champion HS Football Field Turf**
5. **Walk-in Freezer/Coolers & Kitchen Improvements**
6. **District-Wide Roofing**
7. **HVAC Upgrades & Repairs (Curington ES & Cibolo Creek ES)**
8. **Curington and Cibolo Creek Elementary Playgrounds**

2) COMPLETED PROJECTS (In Warranty 2018-2019)

1. **Van Raub ES** – Substantially Complete.
2. **Champion HS Additions & Renovations** – Substantially Complete.
3. **Boerne HS Additions & Renovations** – Substantially Complete.
4. **Boerne MS North Additions & Renovations** – Substantially Complete.
5. **Boerne MS South Additions & Renovations** – Substantially Complete.
6. **HVAC & Controls Upgrades**
 - a. **Pkg. 1 (Kendall ES)** – Substantially Complete.
 - b. **Pkg. 2 (Boerne MS South)** – Phase 1 Substantially Complete.
7. **Site Improvements**
 - a. **Pkg. 1 (Kendall ES & Boerne MS South)** – Substantially Complete.
 - b. **Pkg. 2 (Fair Oaks Ranch ES)** – Substantially Complete.
8. **FORES and Kendall ES Playgrounds** – Substantially Complete.

3) CONSTRUCTION / DESIGN IN PROGRESS

1. **Herff ES** – Structural Steel and Metal deck installation, masonry, interior wall framing, gypsum board and mechanical, electrical and plumbing are in progress. Substantial Completion is scheduled for summer 2019.
2. **Voss Middle School** – Building is completely dried-in. Gypsum Board installation, Tape & Float and Carpentry installation are in progress. Mechanical, Plumbing & Electrical are in progress. Installation of water line to the site and Hwy 46 access are in progress. Substantial Completion is scheduled for summer 2019.
3. **BHS Softball Field Backstop Netting** – Construction in progress. The project is scheduled to be completed in December 2018.
4. **BHS, CHS & BMSS Security Vestibules** – Bid Documents are 50% complete. The project will be bid and awarded in February 2019. Construction is scheduled for summer 2019.

4) SUMMER 2019 PROJECTS (in progress)

1. **Boerne MS South (HVAC & Controls Upgrades)** – Phase 2 HVAC
2. **Boerne MS South Cafeteria** – Ceiling Acoustical Treatment
3. **BHS, CHS & BMSS Security Vestibules** – Upgrades to security entrances

BOND 2016
Monthly Project Status
January 2019

5) VOSS MIDDLE SCHOOL



Site work is in progress



Computer Lab counters being installed



Elevator access at Administration level



Library interior work in progress



Millwork is being installed in humidity controlled spaces.



Classroom Corridor has humidity control. Suspended acoustical ceilings are being installed.


BOND 2016
Monthly Project Status
 January 2019

6) HERFF ELEMENTARY SCHOOL


	
<p>View from upper level parking lot towards parent drop-off.</p>	<p>Bus drop-off view towards Administration and exterior stairs.</p>
	
<p>Structural Steel Installation at vertical circulation.</p>	<p>Stucco and Masonry are in progress.</p>
	
<p>Steel stud framing at the Cafeteria Stage</p>	<p>Taping and Float are in progress at the classrooms</p>

BOND 2016
Monthly Project Status
 January 2019

7) BOERNE HIGH SCHOOL – SECURITY VESTIBULE

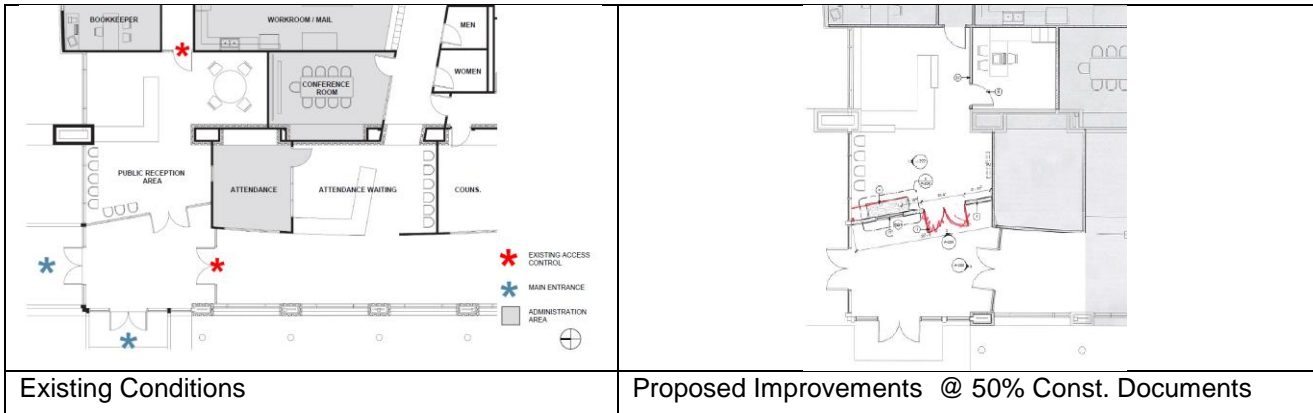

8) CHAMPION HS – SECURITY VESTIBULE

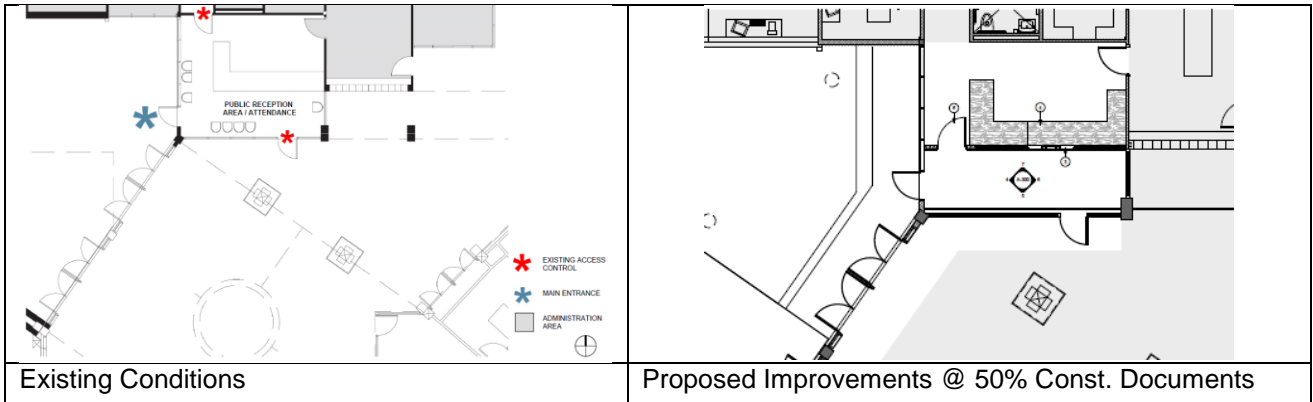

9) BOERNE MS SOUTH – SECURITY VESTIBULE

